



ID	Task Name	Duration	Start	Finish	January 2019														February 2019																	
					16	18	20	22	24	26	28	30	1	3	5	7	9	11	13	15	17	19	21	23	25	27	29	31	2	4	6	8	10	12	14	
1	PRECONSTRUCTION	60 days	Tue 10/16/18	Fri 12/28/18																																
2	Contract Award	1 day	Tue 10/16/18	Tue 10/16/18																																
3	Start Submittals	60 days	Mon 10/22/18	Fri 1/4/19																																
4	Pre-Construction Meeting	1 day	Fri 11/9/18	Fri 11/9/18																																
5	Office Trailer Set up	3 days	Mon 11/12/18	Wed 11/14/18																																
6	Survey Calibration	3 days	Mon 11/19/18	Wed 11/21/18																																
7	Notice To Proceed	1 day	Mon 11/26/18	Mon 11/26/18																																
8	PHASE 1 CALENDAR START	60 days	Mon 11/26/18	Thu 1/24/19																																
9	PHASE 1A & 1B	1 day	Mon 11/26/18	Thu 1/24/19																																
10	Close Taxiway A& B	1 day	Mon 11/26/18	Mon 11/26/18																																
11	Install Erosion Controls	2 days	Mon 11/26/18	Tue 11/27/18																																
12	Clear Area 1A	5 days	Tue 11/27/18	Sat 12/1/18																																
13	Grub Area 1A	4 days	Tue 11/27/18	Fri 11/30/18																																
14	Unclassified Excavation	8 days	Wed 11/28/18	Thu 12/6/18																																
15	Blasting	35 days	Wed 12/5/18	Thu 1/17/19																																
16	Ledge Removal	32 days	Wed 12/12/18	Mon 1/21/19																																
17	Establish Haul Routes	4 days	Mon 12/10/18	Thu 12/13/18																																
18	Process Blasted Ledge	19 days	Wed 1/2/19	Wed 1/23/19																																
19	Place Temp Erosion Controls at end of Phase 1	3 days	Sat 1/19/19	Tue 1/22/19																																
20	SUSPENSION	81 days	Wed 1/23/19	Sat 4/13/19																																
21	PHASE 2 CALENDAR START	60 days	Mon 4/15/19	Thu 6/13/19																																
22	PHASE 2	1 day	Mon 4/15/19	Thu 6/13/19																																
23	Unclassified Excavation	16 days	Mon 4/15/19	Thu 5/2/19																																
24	Underdrain	7 days	Wed 4/17/19	Wed 4/24/19																																
25	Drainage & Basins	3 days	Tue 4/30/19	Thu 5/2/19																																
26	4in Subbase	2 days	Sat 4/20/19	Mon 4/22/19																																
27	Subbase	2 days	Tue 4/23/19	Wed 4/24/19																																
28	Base Gravel	3 days	Thu 4/25/19	Sat 4/27/19																																
29	Finegrade	4 days	Mon 4/29/19	Thu 5/2/19																																
30	Remove Pavement at Taxiway A East	1 day	Thu 4/25/19	Thu 4/25/19																																
31	Test Strip	2 days	Fri 5/3/19	Sat 5/4/19																																
32	Base Pavement	2 days	Mon 5/6/19	Tue 5/7/19																																
33	Electrical	12 days	Wed 4/24/19	Tue 5/7/19																																
34	Loam	12 days	Wed 5/8/19	Tue 5/21/19																																
35	Surface Pavement	2 days	Wed 5/22/19	Thu 5/23/19																																
36	Seed	1 day	Fri 5/24/19	Fri 5/24/19																																
37	Striping	1 day	Mon 6/10/19	Mon 6/10/19																																
38	Sawcut & Seal All Areas	1 day	Tue 6/11/19	Tue 6/11/19																																
39	PHASE 2 MITIGATION AREA	9 days	Sat 4/27/19	Tue 5/7/19																																
40	Install Erosion Controls	1 day	Sat 4/27/19	Sat 4/27/19																																
41	Remove Pavement	3 days	Mon 4/29/19	Wed 5/1/19																																
42	Grade & Place Loam	4 days	Thu 5/2/19	Mon 5/6/19																																

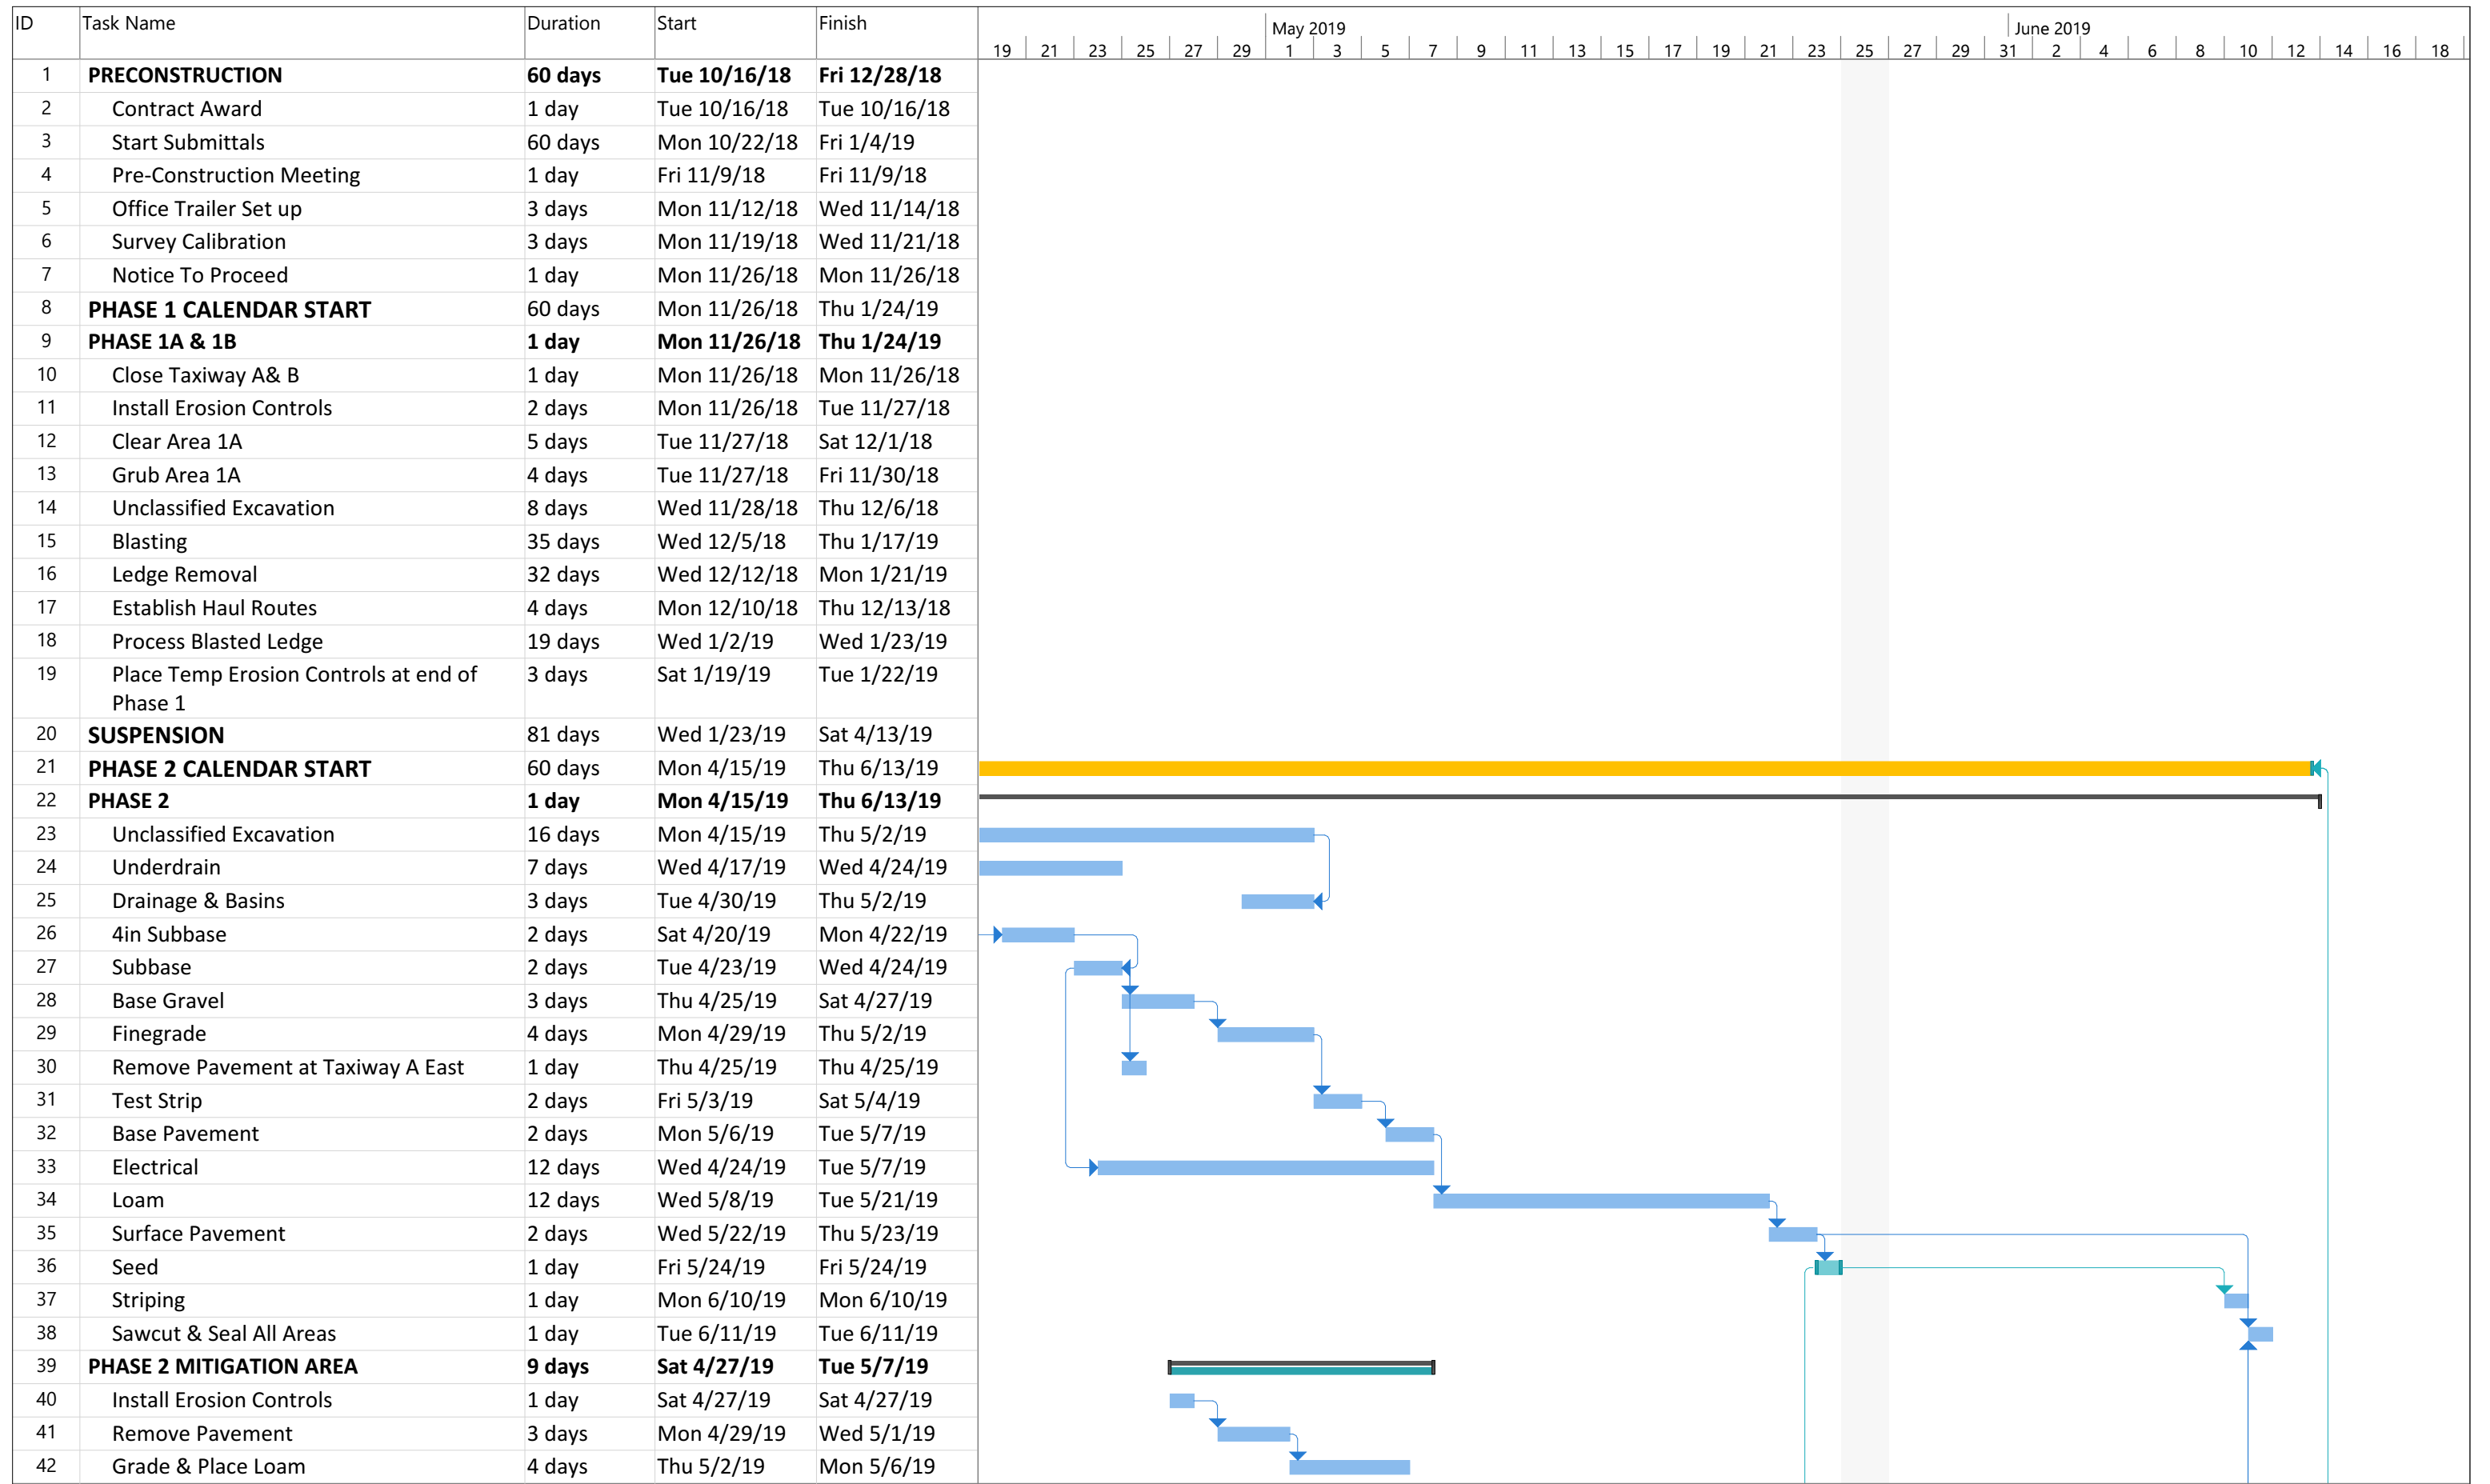

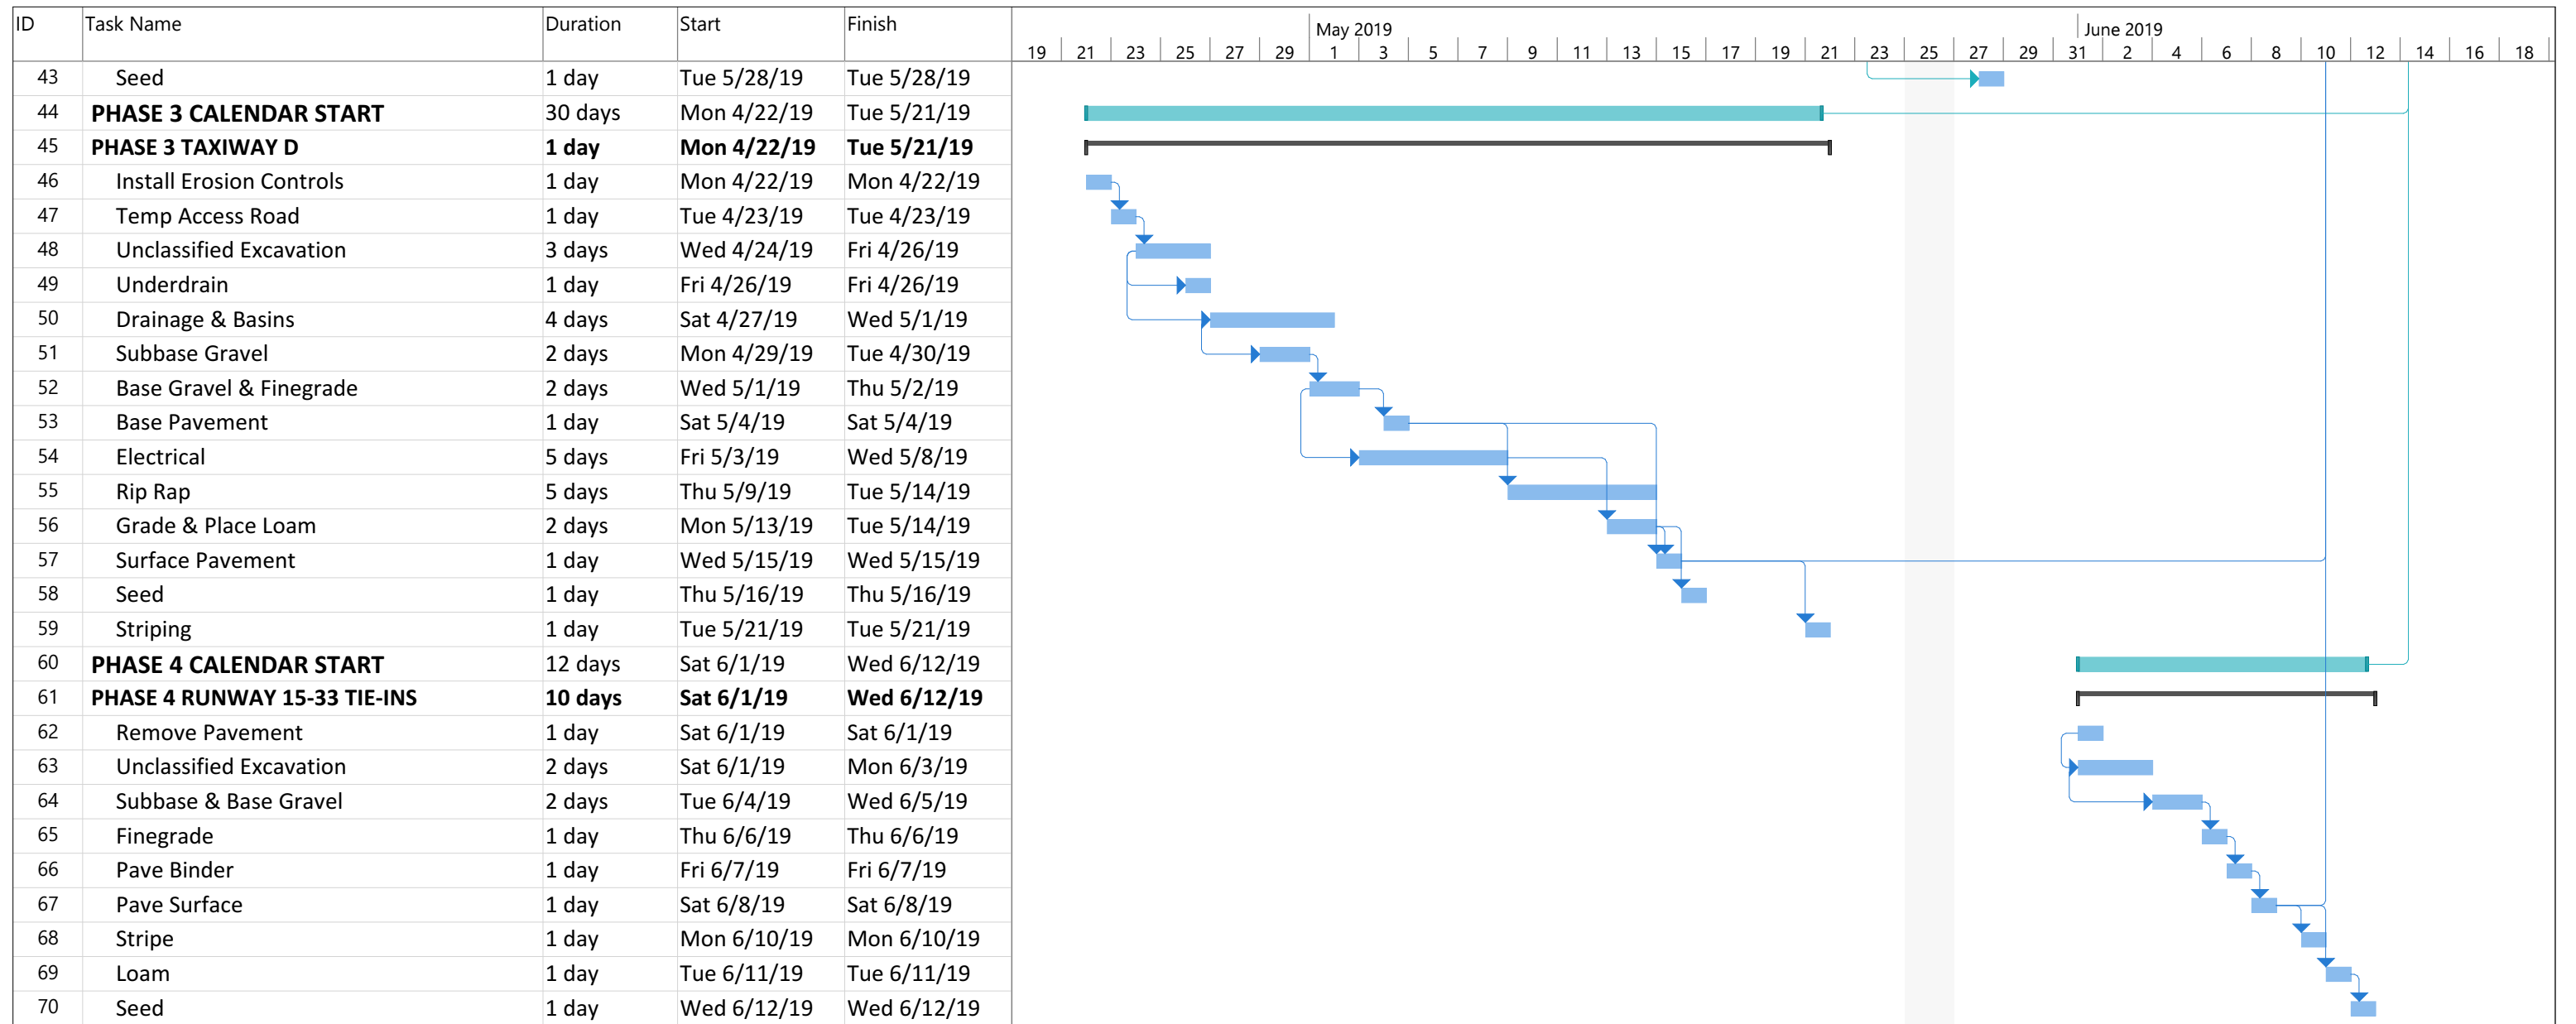

Submittal Number: 4
Revision Number: _____

CONTRACTOR SUBMITTAL FORM (CONTRACTOR)

Job Name: Construct New Runway 15 Partial Parallel Taxiway (Base Bid)
and Runway 33 Bypass Taxiway (Alt No 1)
AIP No. 3-23-0007-XXX-2018
MJ Job No. 18228.01
Contractor: Lane Construction
Address: 655 Main Rd North, Hampden, ME 04444
Contractor's Contact: Wayne Watson Phone Number: 207-307-7949
Reviewed By: TJ Coyle Date Submitted: 11-2-18
 Check here if submittal is from a Subcontractor
Item No.: M-100
Specification Section and Paragraph: M-001-1.15

CERTIFICATION

I HEREBY CERTIFY that the attached submittal has been reviewed under the terms of the Contract Documents and is in conformity with the requirements of the Plans and Specifications unless specifically noted otherwise. It is understood that the Contractor is responsible for dimensions and quantities to be confirmed and correlated at the site, for information that pertains solely to the fabrication process or to the means, methods, techniques, sequences and procedures of construction, and for coordination of the Work of all trades.

- 1- Submitted as specified
- 2 - Submitted "AS EQUAL" to the product specified
- 3 - Submitted "IN SUBSTITUTION" to the product specified
- 4 - Subcontractor submittal form included
- 5 - Other

Description of Submittal Components: Overall Work Schedule

Submittal will not be approved without an acceptable Form MJ-212 "Contractor / Subcontractor /
Supplier Buy American Certification."

(For additional comments attach and number additional pages)
